




	Facts	
Donor	American Red Cross	
Implementing	United Nations Office for Project	
agency	Services (UNOPS)	
Awarded amount	\$ 6,842,941 (total for ARC	
	project)	The state of the s
Project Goal	Strengthen humanitarian	
	assistance to Haitian	Minimal
	communities affected by the	
	earthquake contributing to the	and the second s
	recovery of the country.	AND DESCRIPTION OF THE PARTY OF
Project duration	12 months (3 months at	
	Villambetta, including site prep)	Achievements
Project activities	<ul> <li>Construction of 1500         transitional shelters</li> <li>Construction of 600 latrines</li> <li>Installation of 1500 water         catchment systems</li> </ul>	<ul> <li>A total of 1500 shelters constructed with 293 on two transitional sites (Villambeta: 220 and Carvil: 73) and 1207 in the Neighborhood</li> <li>606 latrines constructed with 145 on transitional sites</li> <li>Installed 1500 water catchment systems with 293 at transitional sites</li> </ul>
Beneficiaries	Direct beneficiaries include 1500 affected families, or approximately 4500 individuals. Indirect beneficiaries include some 88 skilled and unskilled labourers to help produce and construct the transitional shelters and water and sanitation facilities	<ul> <li>Total Beneficiaries: 8150</li> <li>Direct Beneficiaries: 1500</li> <li>Indirect Beneficiaries: 6650 (with 100 people trained with carpentry skills)</li> <li>Male: 46%</li> <li>Females: 54%</li> <li>Minors: 11%</li> <li>Elderly: 3.95%</li> </ul>



**UNOPS-American Red Cross Shelter locations** 

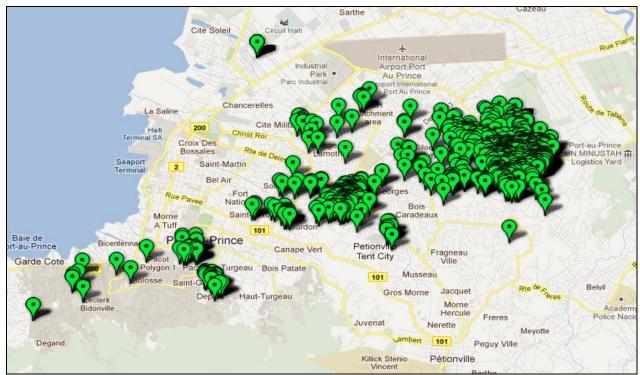

Carvil: Community gathering at Carvil for hand over the site to communities along colleagues from American Red Cross



Camp Carvil: UNOPS Mitigation team making drainage around the new transitional site



Villambeta: A child on the first day of his new house after spending 18 months in a camp



Carvil: During construction.
